Tiburon Team Legacy frac (Ascent water share) - J Bar J staging plan

Staging: J Bar J pad, 25204 Oxford Rd, Quaker City, OH 43773 (40.032239, -81.263992) · **CB 27**

This document is designed to clearly set expectations for using the J Bar J pad for staging and transportation of re-use water to the Tiburon – Team Legacy frac op.

Select will provide manpower at the J Bar J pad to manage trucks and truck traffic in and out of the J bar J pad as well as traffic heading over to the Tiburon, Team Legacy frac job.

Light plants and porta johns will be installed as necessary during operations.

Production water will arrive on pad and follow designated traffic flow for operation.

Speed limit on J bar J lease road will be a maximum of 10MPH. All posted Ascent and Tiburon speed limits as well as community speed limits are to be strictly observed.

Engine Braking is prohibited on Ipswitch Road.

All PPE, chock blocks, and EHS practices and standards will be observed by all personnel on pad.

Absolutely no smoking will be allowed on pad.

A minimum 35’ buffer will be maintained for all equipment while driving on pad.

No personnel will be allowed near production equipment except Ascent lease operators and water trucks loading from production tanks.

Cameras are working on pad and will be checked periodically to ensure rules are being followed.

Any trash on pad/grading that needs done due to increased traffic will be managed by water department and production foreman when frac operations are complete.

Personal gas detection is required for all personnel.

Any incidents, near misses, or stop work situations will be immediately reported to Ascent representatives.

Production is ALLOWING us to utilize their site to improve our operations. This is a privilege, and it needs to be stressed that if we do not follow the above requirements, we could lose the privilege.

Expected daily truck traffic on pad100-140 trucks per Shift.

Completions Dept. Representative_____

Production Dept. Representative_____

Water Dept. Representative _____Casey Seyerle – Foreman_____

Haul route to J Bar J staging

Google Maps

22995 Oxford Rd, Quaker City, OH 43773 to
25204 Oxford Rd, Quaker City, OH 43773

Drive 2.6 miles, 4 min



Imagery ©2026 Airbus, CNES / Airbus, Maxar Technologies, USDA/FPAC/GEO, Map data ©2026 1000 ft

22995 Oxford Rd
Quaker City, OH 43773


1. Head toward Oxford Rd
89 ft
2. Turn left onto Oxford Rd
1.0 mi
3. Continue onto Pisgah Rd
0.1 mi
4. Slight left onto Oxford Rd
Destination will be on the right
1.4 mi

25204 Oxford Rd
Quaker City, OH 43773

J Bar J staging to Tiburon Team Legacy pad

Google Maps

40.0322827, -81.2638465 to Tiburon - Legacy Pad, 61978 Willow Rd, Quaker City, OH 43773 Drive 6.5 miles, 12 min

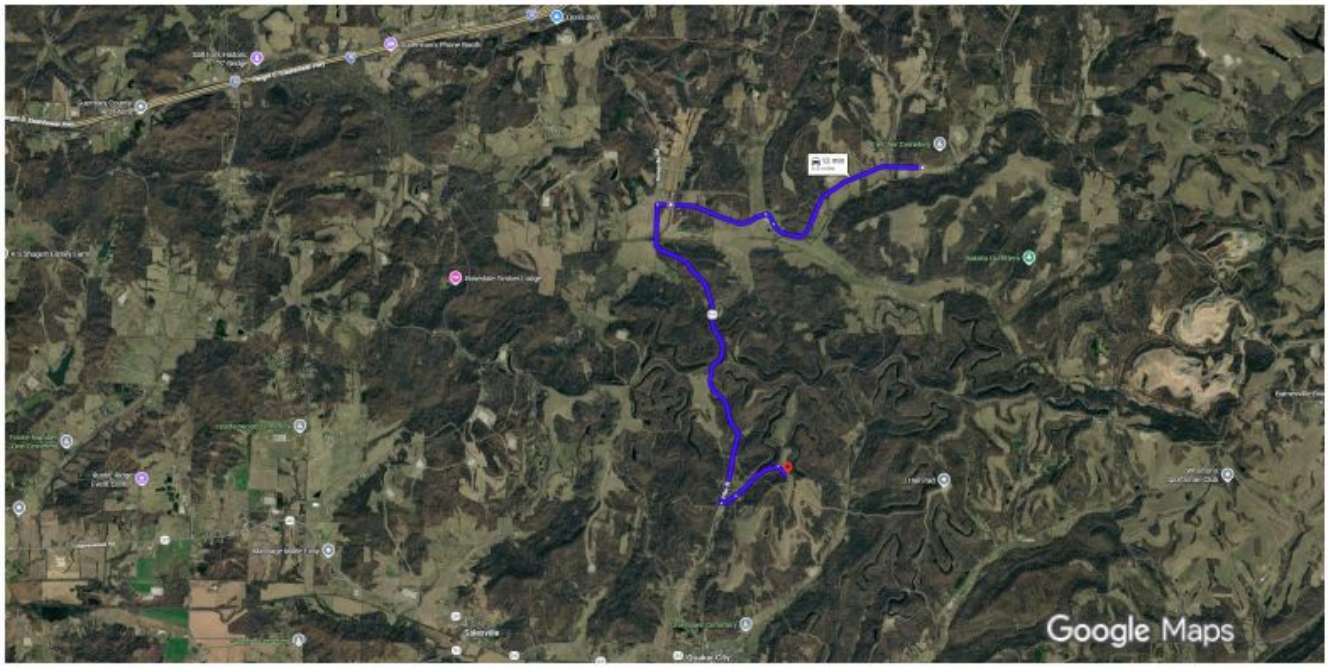

Imagery ©2026 Airbus, CNES / Airbus, Landsat / Copernicus, Maxar Technologies, USDA/FPAC/GEO, Map data ©2026 Google 2000 ft

40.0322827, -81.2638465

1. Head toward Wilderness Ln — 1.6 mi
2. Continue onto Pisgah Rd — 0.1 mi
3. Continue straight onto Oxford Rd — 1.0 mi
4. Turn left onto OH-513 S — 3.0 mi
5. Turn left onto Ipswitch Ln — 0.1 mi
6. Continue onto Willow Rd — 0.5 mi
7. Turn right onto Fulcrum Rd — 499 ft

Tiburon - Legacy Pad
61978 Willow Rd, Quaker City, OH 43773

J Bar J staging layout

